

## Construction Update - August 14, 2024

### STORM SEWER INSTALLATION CONTINUES

Storm sewer installation continues down the centerline of Arlington Heights Road. While the project is in Stage 1, traffic on Arlington Heights Road has been shifted to the outside lanes only with one lane remaining open in each direction. This will remain in place for the next few months until the centerline storm sewer work is complete on Arlington Heights Road from Lake Cook Road to IL83.

Stage 2 will shift both northbound and southbound traffic to the east side of Arlington Heights Road so the storm sewer and road work can be completed on the west side.


The storm outfall manhole at the north side of Buffalo Creek was installed and storm sewer installation continued north past Bernay Lane. A second crew worked from Checker Road to Bernay Lane, connecting the lateral lines into the mainline structures.

This week the storm sewer installation will begin north from Brittany Lane in the centerline while the second crew installs the lateral storm sewer lines into the mainline sewer.

Occasional daily shifts to an inside lane will be used as needed to accomplish the storm sewer or utility relocation work. Please use caution when traveling through the area.



*Storm sewer installation*

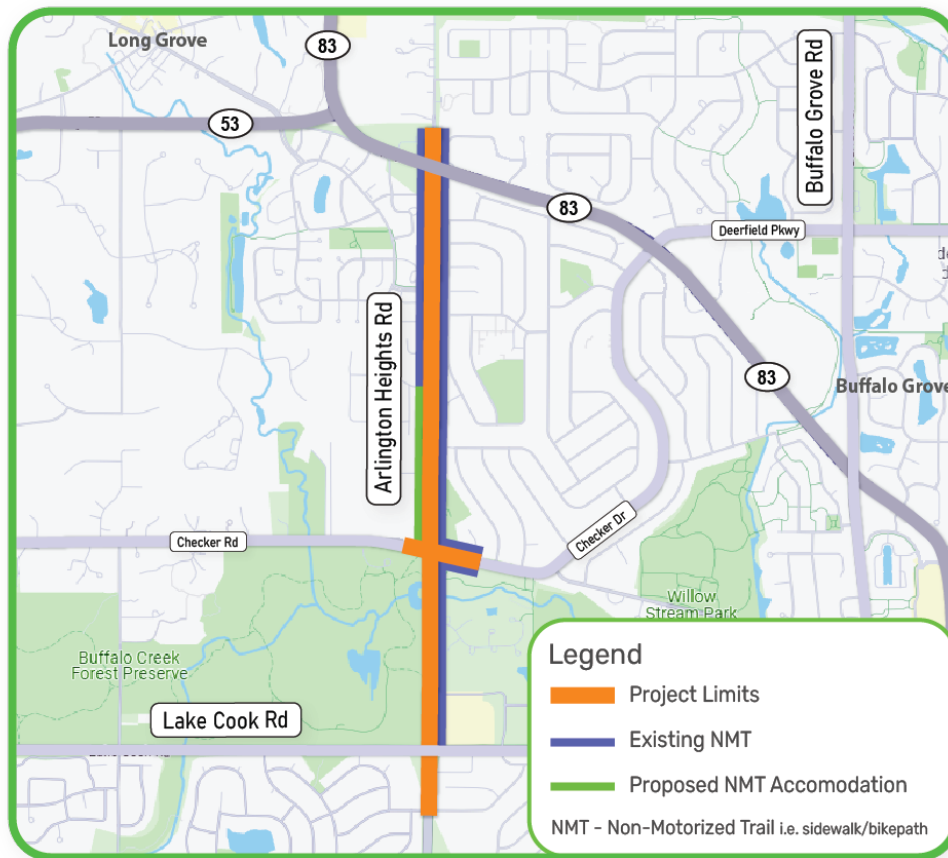

**Christopher B. Burke Engineering, Ltd.**  
Kevin Betke, Construction Engineer  
847-833-0252  
[kbetke@cbbel.com](mailto:kbetke@cbbel.com)

600 W Winchester Rd  
Libertyville, Illinois 60048  
Julian Rozwadowski, P.E. Project Manager  
847-377-7506

METRO STRATEGIES GROUP | 1901 Butterfield Rd., Suite 260 | Downers Grove, IL 60515  
US

[Unsubscribe](#) | [Update Profile](#) | [Constant Contact Data Notice](#)



Try email marketing for free today!
