



Construction Update - October 21, 2024

CHANGE IN TRAFFIC THIS WEEK!

Last week, the contractor finished a majority of the Stage 1 storm sewer installation along the centerline of Arlington Heights Road. There are still several areas remaining that will be completed after the watermain work is done.

This week, beginning on Monday, October 21st, the contractor will begin relocating the watermain in the following locations along Arlington Heights Road:

- Bernay Lane
- Carlton Place
- Alden Lane


Relocating the watermain will take approximately three weeks and any changes to traffic flow will be shared in future updates as soon as they are scheduled.

Please note that on Tuesday, October 22nd, traffic on Arlington Heights Road will be shifted to the east side of the road from Bernay Lane to Lake Cook Road so sewer and road improvements can be completed.

Please use caution when traveling through the area to support a safe work environment.



Storm laterals installation

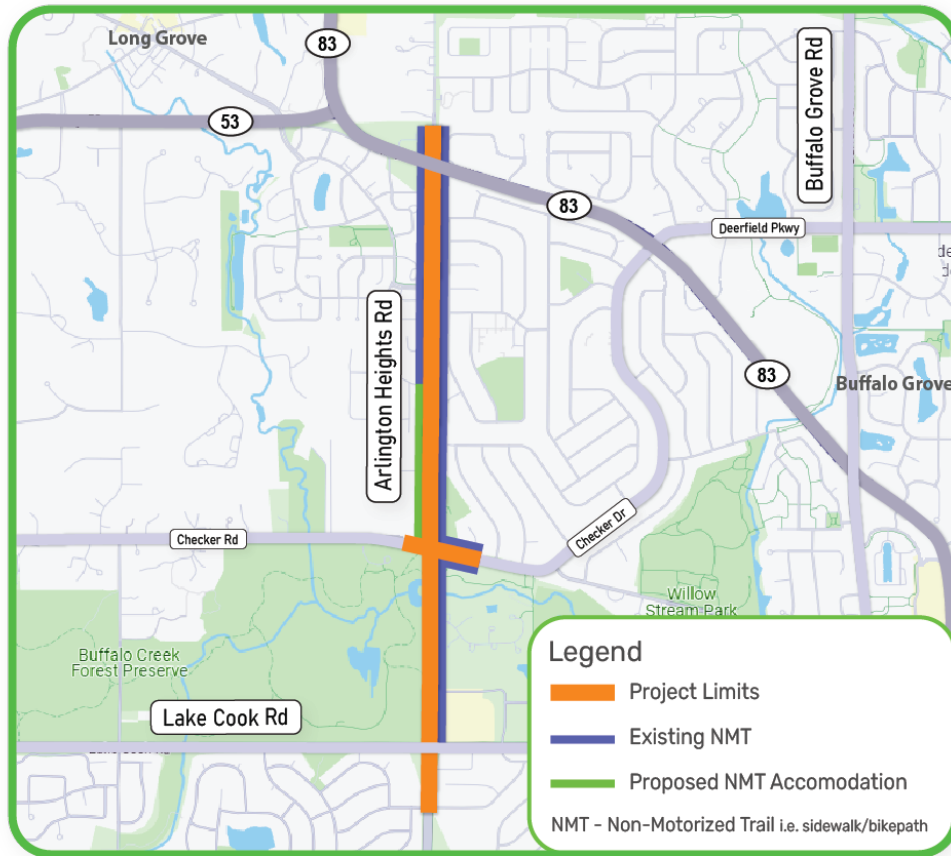



Christopher B. Burke Engineering, Ltd.
Kevin Betke, Construction Engineer
847-833-0252
kbetke@cbbel.com

600 W Winchester Rd
Libertyville, Illinois 60048
Julian Rozwadowski, P.E. Project Manager
847-377-7506

METRO STRATEGIES GROUP | 1901 Butterfield Rd., Suite 260 | Downers Grove, IL 60515
US

[Unsubscribe](#) | [Update Profile](#) | [Constant Contact Data Notice](#)



Try email marketing for free today!
